ID		Task Mode	Task Name	Duration	Start	Finish
1			**OWEN SOUND LAB FLOORING REPLACEMENT**	**124 days**	**Tue 3/12/24**	**Fri 8/30/24**
2			**RFQ for Construction (Phase 1 & 2)**	**0 days**	**Tue 3/12/24**	**Tue 3/12/24**
3			RFQ development	9 days	Fri 3/15/24	Wed 3/27/24
4			RFQ	24 days	Mon 4/08/24	Thu 5/09/24
5			Contractor walk through	1 day	Wed 4/17/24	Wed 4/17/24
6			Contractor Selection & Award	6 days	Thu 5/16/24	Thu 5/23/24
7			Construction kick off meeting	1 day	Wed 6/05/24	Wed 6/05/24
8			Mobilization	5 days	Mon 7/08/24	Fri 7/12/24
9			**Phase 1 Completion**	**25 days**	**Mon 7/15/24**	**Fri 8/16/24**
10			Phase 1A	5 days	Mon 7/15/24	Fri 7/19/24
11			Phase 1B - Ravens Studio Install is July 29	5 days	Mon 7/22/24	Fri 7/26/24
12			Phase 1B - Furniture Install	3 days	Mon 7/29/24	Wed 7/31/24
13			Phase 1C	5 days	Mon 8/05/24	Fri 8/09/24
14			Phase 1D - Weekend Work	2 days	Fri 8/09/24	Mon 8/12/24
15			Phase 1E	5 days	Mon 8/12/24	Fri 8/16/24
16			**Phase 2 Completion**	**10 days**	**Mon 8/19/24**	**Fri 8/30/24**
17			Phase 2a	5 days	Mon 8/19/24	Fri 8/23/24
18			Phase 2b	5 days	Mon 8/26/24	Fri 8/30/24

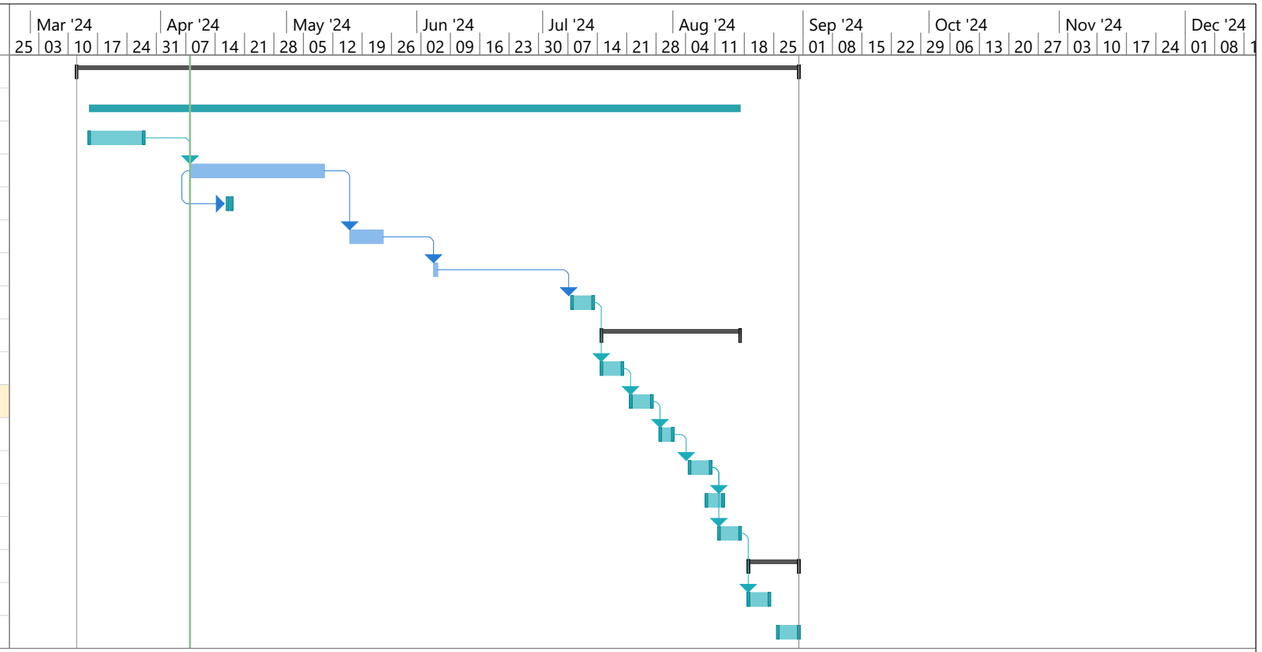

Project: Lab Flooring - Apr 08, 2
Date: Mon 4/08/24

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	
